


PRODUCTION PERFORMANCE & QUALITY REPORT

Facility: Main Manufacturing Plant Reporting Period: Weekly Summary

Executive Summary:

During the weekly reporting period, total production output reached 8,690 units against an aggregated target of 8,700, representing a 99.8% target realization. While Overall Equipment Effectiveness (OEE) remained strong on Lines A and B, Line C experienced minor calibration issues that depressed its OEE to 78.3%. Quality metrics highlighted a total of 364 rejections, with Shift 3 (Night) exhibiting a heightened defect rate of 6.0% primarily driven by dimensional deviations. Corrective actions have been scheduled for immediate tool recalibration on Line C and targeted operator training to address these local inefficiencies.

1. Weekly Production Trends

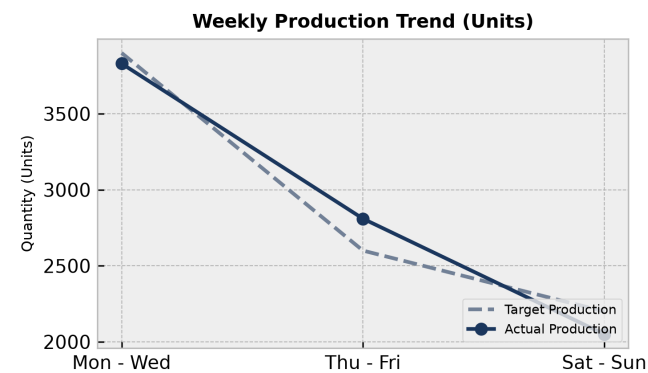

Production Analysis:

Daily output trends show high stability during mid-week operations, with peak efficiency achieved during the Thursday-Friday window, producing 2,810 units and exceeding the 2,600 target. However, weekend shifts (Saturday-Sun) saw a minor drop to 2,050 units against a 2,200 target due to reduced staffing levels and longer changeover times. Monday to Wednesday performance was consistent, nearly meeting the target of 3,900 with 3,830 completed units.


Day	Target	Actual	Status
Mon - Wed	3900	3830	On Track
Thu - Fri	2600	2810	Exceeded
Sat - Sun	2200	2050	Below Target

2. Machine Performance (OEE Breakdown)


OEE Overview:

Equipment performance varied across the main production lines. Lines A and B maintained optimal performance levels with OEE scores of 88.5% and 92.0% respectively, exceeding the world-class threshold of 85%. Line C fell below the target threshold at 78.3% due to frequent micro-stoppages and tool wear, classifying its operational health as Needs Review.

Line	OEE Score	Status
Line A	88.5%	Optimal
Line B	92.0%	Optimal
Line C	78.3%	Needs Review

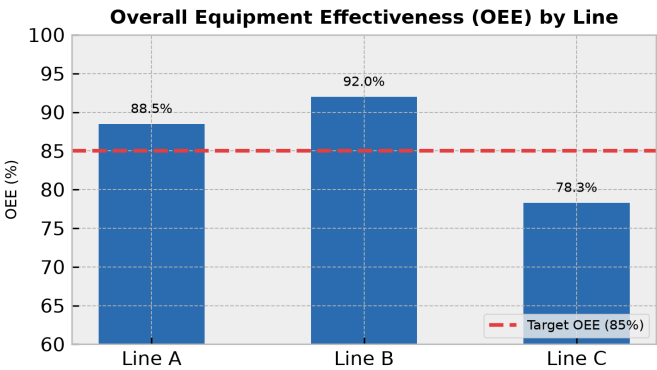

3. Rejection vs. Production Volume by Shift

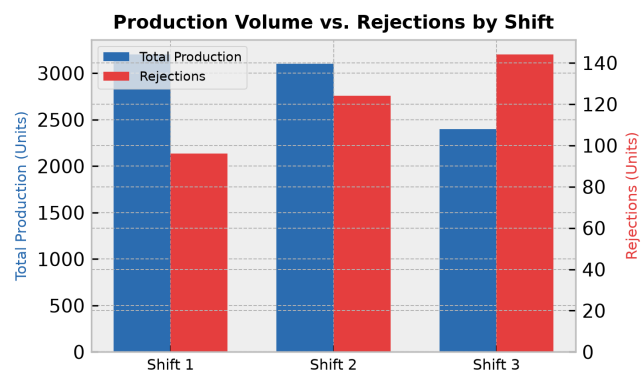

Shift Efficiency Analysis:


Shift performance analysis reveals a clear correlation between operating hours and defect rates. Shift 1 (Day) recorded the highest output at 3,200 units with a low 3.0% defect rate. In contrast, Shift 3 (Night) produced 2,400 units but suffered from an elevated defect rate of 6.0% (144 rejections), pointing to reduced supervision and fatigue-related process drift during early morning hours.

Shift	Output	Rejections	Defect Rate
Shift 1 (Day)	3200	96	3.0%
Shift 2 (Eve)	3100	124	4.0%
Shift 3 (Night)	2400	144	6.0%

4. Scrap Analysis & Waste Distribution

Key Scrap Drivers:

Dimensional deviations remain the leading driver of material scrap, accounting for 42.0% of all rejected parts, which aligns with the tooling issues flagged on Line C. Surface defects contributed to 28.0% of scrap, typically occurring during high-temperature extrusion phases, while material flaws and other general assembly errors accounted for 10.0% and 20.0% respectively.

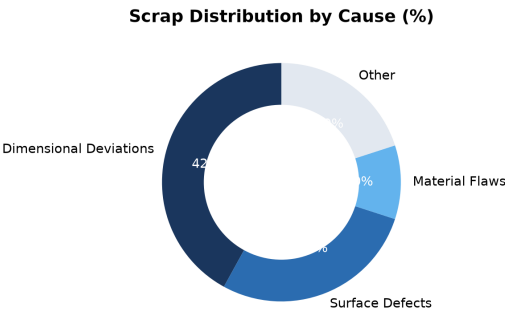

5. Corrective Action Plan

Action Item	Target Area	Owner	Deadline
Recalibrate tooling and guide rails on Line C	Line C	Maintenance	Aug 14, 2026
Conduct refresher training on dimensional tolerance checks for Shift 3 operators	Shift 3	Operations	Aug 18, 2026
Perform preventive maintenance on high-temperature extrusion nozzles	Line B	Engineering	Aug 21, 2026
