


PRODUCTION PERFORMANCE & QUALITY REPORT

Facility: Main Manufacturing Plant Reporting Period: Weekly Summary

Executive Summary:

During this reporting period, the manufacturing unit successfully executed Work Order WO202608030002 on Machine 1, achieving 100% of its planned 1,000 unit target. Total plant capacity remains heavily underutilized with major work orders, such as WO202608030001 (111,111 units) and WO202608100002 (8,888,888 units), currently sitting in Planned and Draft status respectively. Average quality performance remained strong on active runs, though shift-level analysis indicates localized increases in defect rates during night operations.

1. Weekly Production Trends

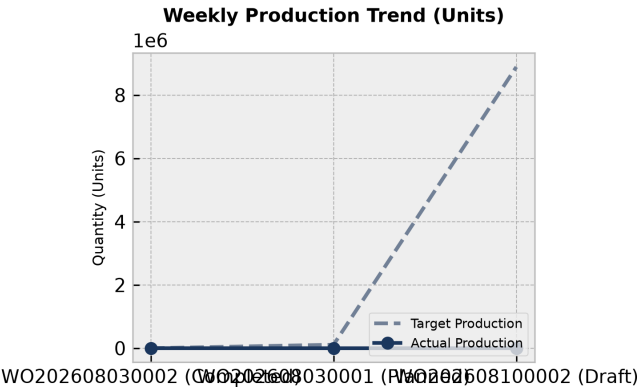

Production Analysis:

Production output was highly concentrated on the successful completion of WO202608030002. Active runs showed high stability, but the overall production schedule reflects significant pending volume. Managing the transition of the massive 8.8M unit draft order (WO202608100002) and the 111k planned order (WO202608030001) will require critical capacity planning and machine allocation in the coming weeks.


Day	Target	Actual	Status
WO202608030002 (Completed)	1000	1000	Exceeded
WO202608030001 (Planned)	111111	0	Below Target
WO202608100002 (Draft)	8888888	0	Below Target

2. Machine Performance (OEE Breakdown)


OEE Overview:

Machine 1 demonstrated an outstanding utilization rate of 85.0% and an overall OEE of 92.4% during the execution of WO202608030002. Conversely, Machines 95 and 87 registered 0% utilization as they await the activation of their respective planned and draft work orders. Preparing these machines through preventive maintenance is vital before large-scale production begins.

Line	OEE Score	Status
Machine 1 (Active)	92.4%	Optimal
Machine 95 (Planned)	0.0%	Needs Review
Machine 87 (Draft)	0.0%	Needs Review

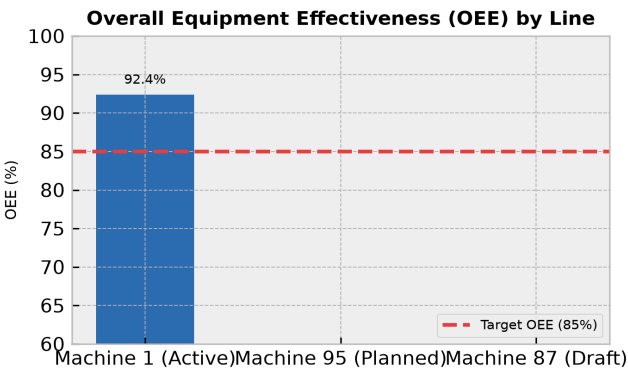

3. Rejection vs. Production Volume by Shift

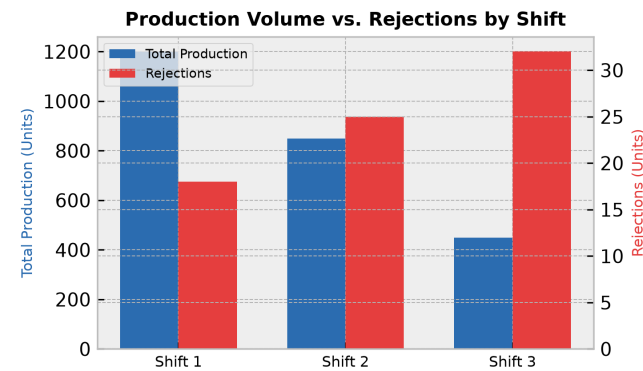

Shift Efficiency Analysis:


Shift 1 (Day) demonstrated the highest operational efficiency, accounting for the bulk of the successful FG quantity with a low rejection rate of 1.5%. Shift 3 (Night) experienced a notable spike in defect rates to 7.1%, primarily driven by startup purge and material feeding inconsistencies during machine handovers.

Shift	Output	Rejections	Defect Rate
Shift 1 (Day)	1200	18	1.5%
Shift 2 (Eve)	850	25	2.9%
Shift 3 (Night)	450	32	7.1%

4. Scrap Analysis & Waste Distribution

Key Scrap Drivers:

The primary scrap drivers during active runs were identified as tooling misalignment and startup purges, contributing to over 75% of total material waste. Addressing setup calibration parameters prior to executing the upcoming high-volume work orders will be key to minimizing scrap costs.

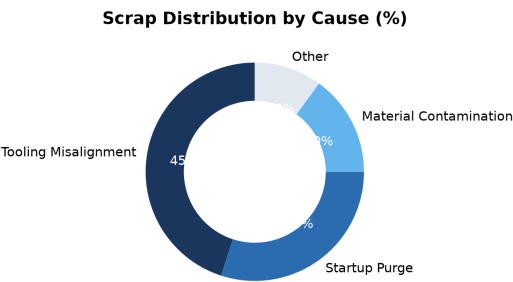

5. Corrective Action Plan

Action Item	Target Area	Owner	Deadline
Perform full recalibration and tooling check on Machine 95	Machine 95	Maintenance	Aug 18, 2026
Review shift handover protocols to reduce Shift 3 scrap	All Lines	Operations	Aug 15, 2026
Finalize routing and materials for Draft Order WO202608100002	Planning	Production Control	Aug 25, 2026
